ID	Task Name	Duration	Start
1			
2	STM End	0w	23 Oct '96
3	EM End	0w	31 Mar '97
4	QM End	0w	14 May '97
5	FM End	0w	15 Mar '98
6	FS End	0w	15 May '98
7			
8	STM Ext-Harn build	5w	19 Sep '96
9			
10	EM START	0w	19 Sep '96
11			
12	EM BPE Camera layout	1.5w	19 Sep '96
13	EM BPE Process layout	1.5w	30 Sep '96
14	EM BPE Darray layout	1.5w	10 Oct '96
15	EM BPE Lookup layout	1.5w	21 Oct '96
16	EM BPE Selector layout	1.5w	31 Oct '96
17	EM BPE Monitor layout	1.5w	11 Nov '96
18	EM BPE Mother layout	1.5w	21 Nov '96
19	EM BPE Fliter A layout	1.5w	2 Dec '96
20	EM BPE Filter B layout	1.5w	12 Dec '96
21	EM BPE Camera assembly	1w	30 Sep '96
22	EM BPE Process assembly	1w	10 Oct '96
23	EM BPE Darray assembly	1w	21 Oct '96
24	EM BPE Lookup assembly	1w	31 Oct '96
25	EM BPE Selector assembly	1w	11 Nov '96
26	EM BPE Monitor assembly	1.5w	21 Nov '96
27	EM BPE Mother assembly	1.5w	2 Dec '96
28	EM BPE Filter A assembly	2d	12 Dec '96
29	EM BPE Filter B assembly	2d	23 Dec '96
30			
31	EM HVPSU brd1 assembly	1w	24 Oct '96
32	EM HVPSU brd2 assembly	1w	31 Oct '96
33	EM HVPSU brd3 assembly	1w	7 Nov '96
34	EM HVPSU brd4 assembly	1w	14 Nov '96
35	EM HVPSU brd5 assembly	1w	21 Nov '96
36			
37	EM Int-Harn build	6w	28 Nov '96
38	EM Ext-Harn build	4w	9 Jan '97
39	EM EGSE assembly	2w	6 Feb '97
40			
41	QM START	0w	12 Dec '96
42			
43	QM HVPSU updates	4w	23 Dec '96
44	QM BPE updates	7w	20 Jan '97
45	BCH Radiation Test boards	2w	10 Mar '97
46	QM EGSE layout	3w	24 Mar '97
47			
48	QM BCH assembly	3w	25 Dec '96
49	QM BPE assembly (9)	9w	15 Jan '97
50	QM HVPSU assembly (9)	7.5w	19 Mar '97
51	QM Int-Harn build	4w	20 Feb '97
52	QM Ext-Harn build	3w	20 Mar '97
53	QM EGSE assembly	2w	10 Apr '97
54	QM Test Harnesses	3w	24 Apr '97
55			
56	FM START	0w	21 Mar '97
57			
58	FM ICU updates	4w	14 Apr '97
59	FM BCH updates	3w	12 May '97
60	FM HVPSU updates	4w	2 Jun '97
61	FM BPE updates (2)	5w	30 Jun '97
62			
63	FM ICU assembly (5)	5w	15 May '97
64	FM BCH assembly (3)	3w	19 Jun '97
65	FM HVPSU assembly (5)	7w	10 Jul '97
66	FM BPE assembly (9)	9w	28 Aug '97
67	FM ICU assembly (5)	5w	30 Oct '97
68	FM BPE assembly (9)	9w	4 Dec '97
69	FM Int-Harn build	6w	12 May '97
70	FM Ext-Harn build	5w	23 Jun '97
71	FM Test Harnesses	2w	28 Jul '97
72	FM BCH assembly (3)	3w	11 Aug '97
73	FM HVPSU assembly (5)	7w	1 Sep '97
74	FM EGSE assembly	2w	20 Oct '97
75			
76	FS ICU assembly (5)	5w	3 Nov '97
77	FS BCH assembly (3)	3w	8 Dec '97
78	FS HVPSU assembly (5)	7w	29 Dec '97
79	FS BPE assembly (9)	9w	16 Feb '98

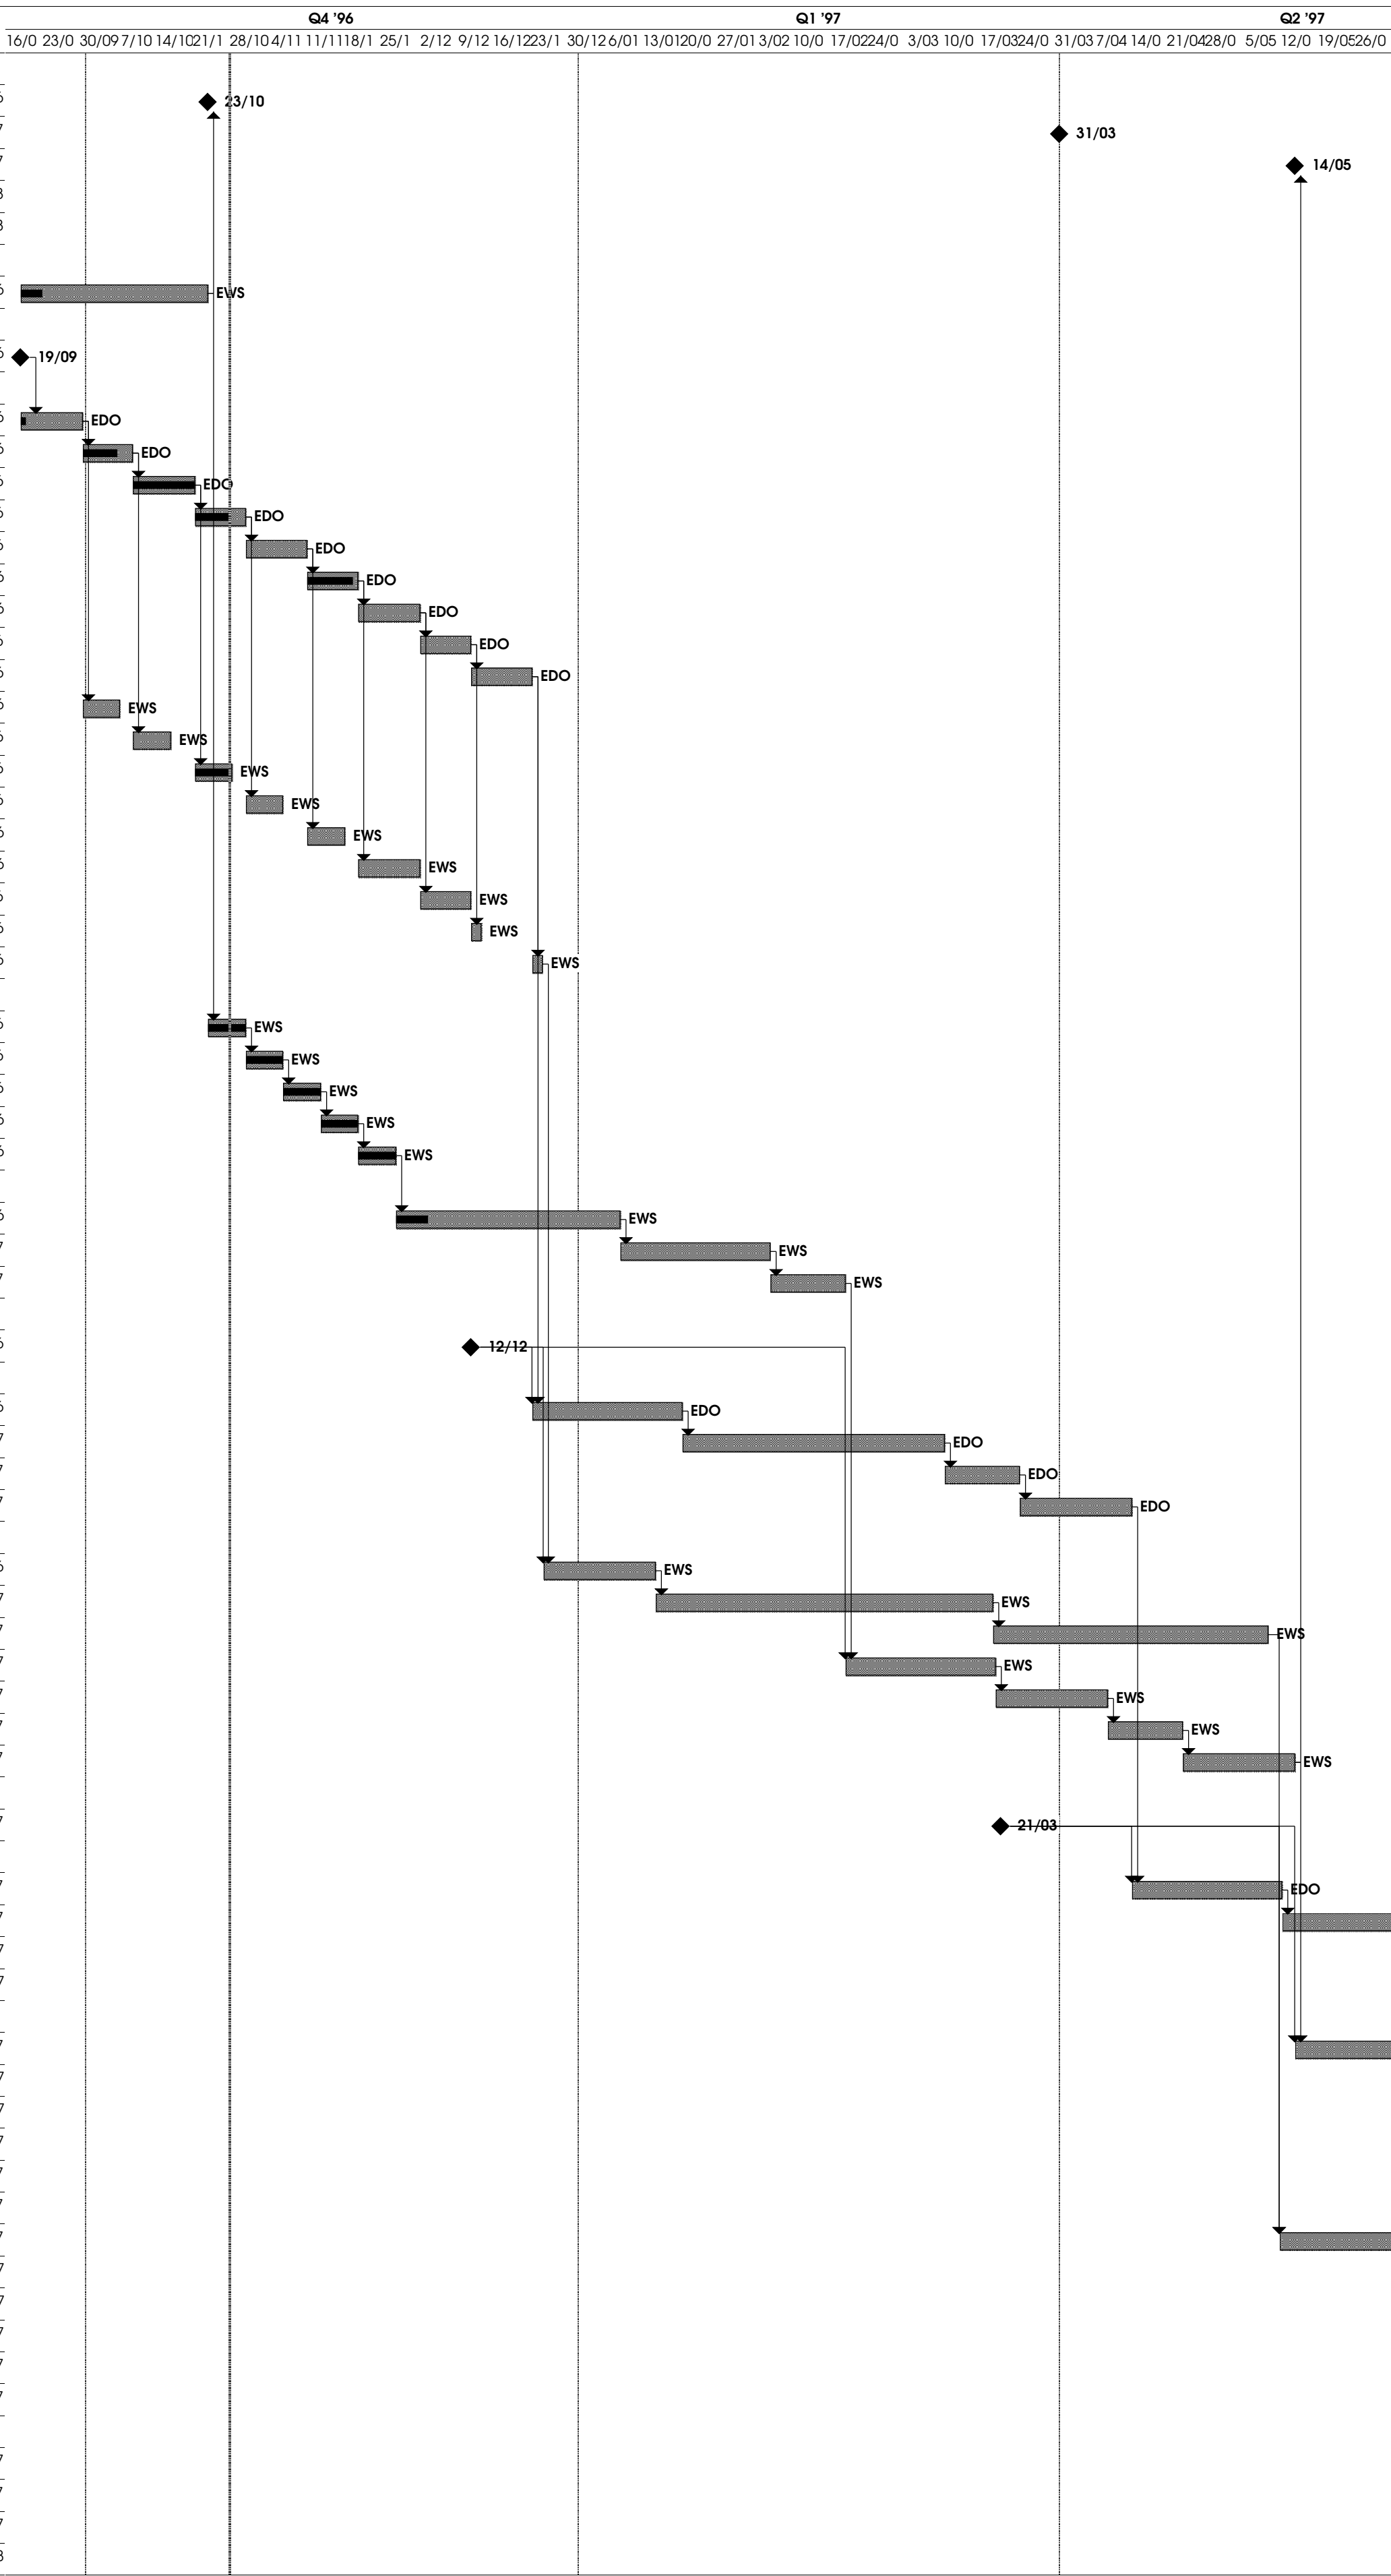

Project: XMM-OM Combined EDO and EWS
Date: 28 Oct '96

Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Milestone | Rolled Up Progress

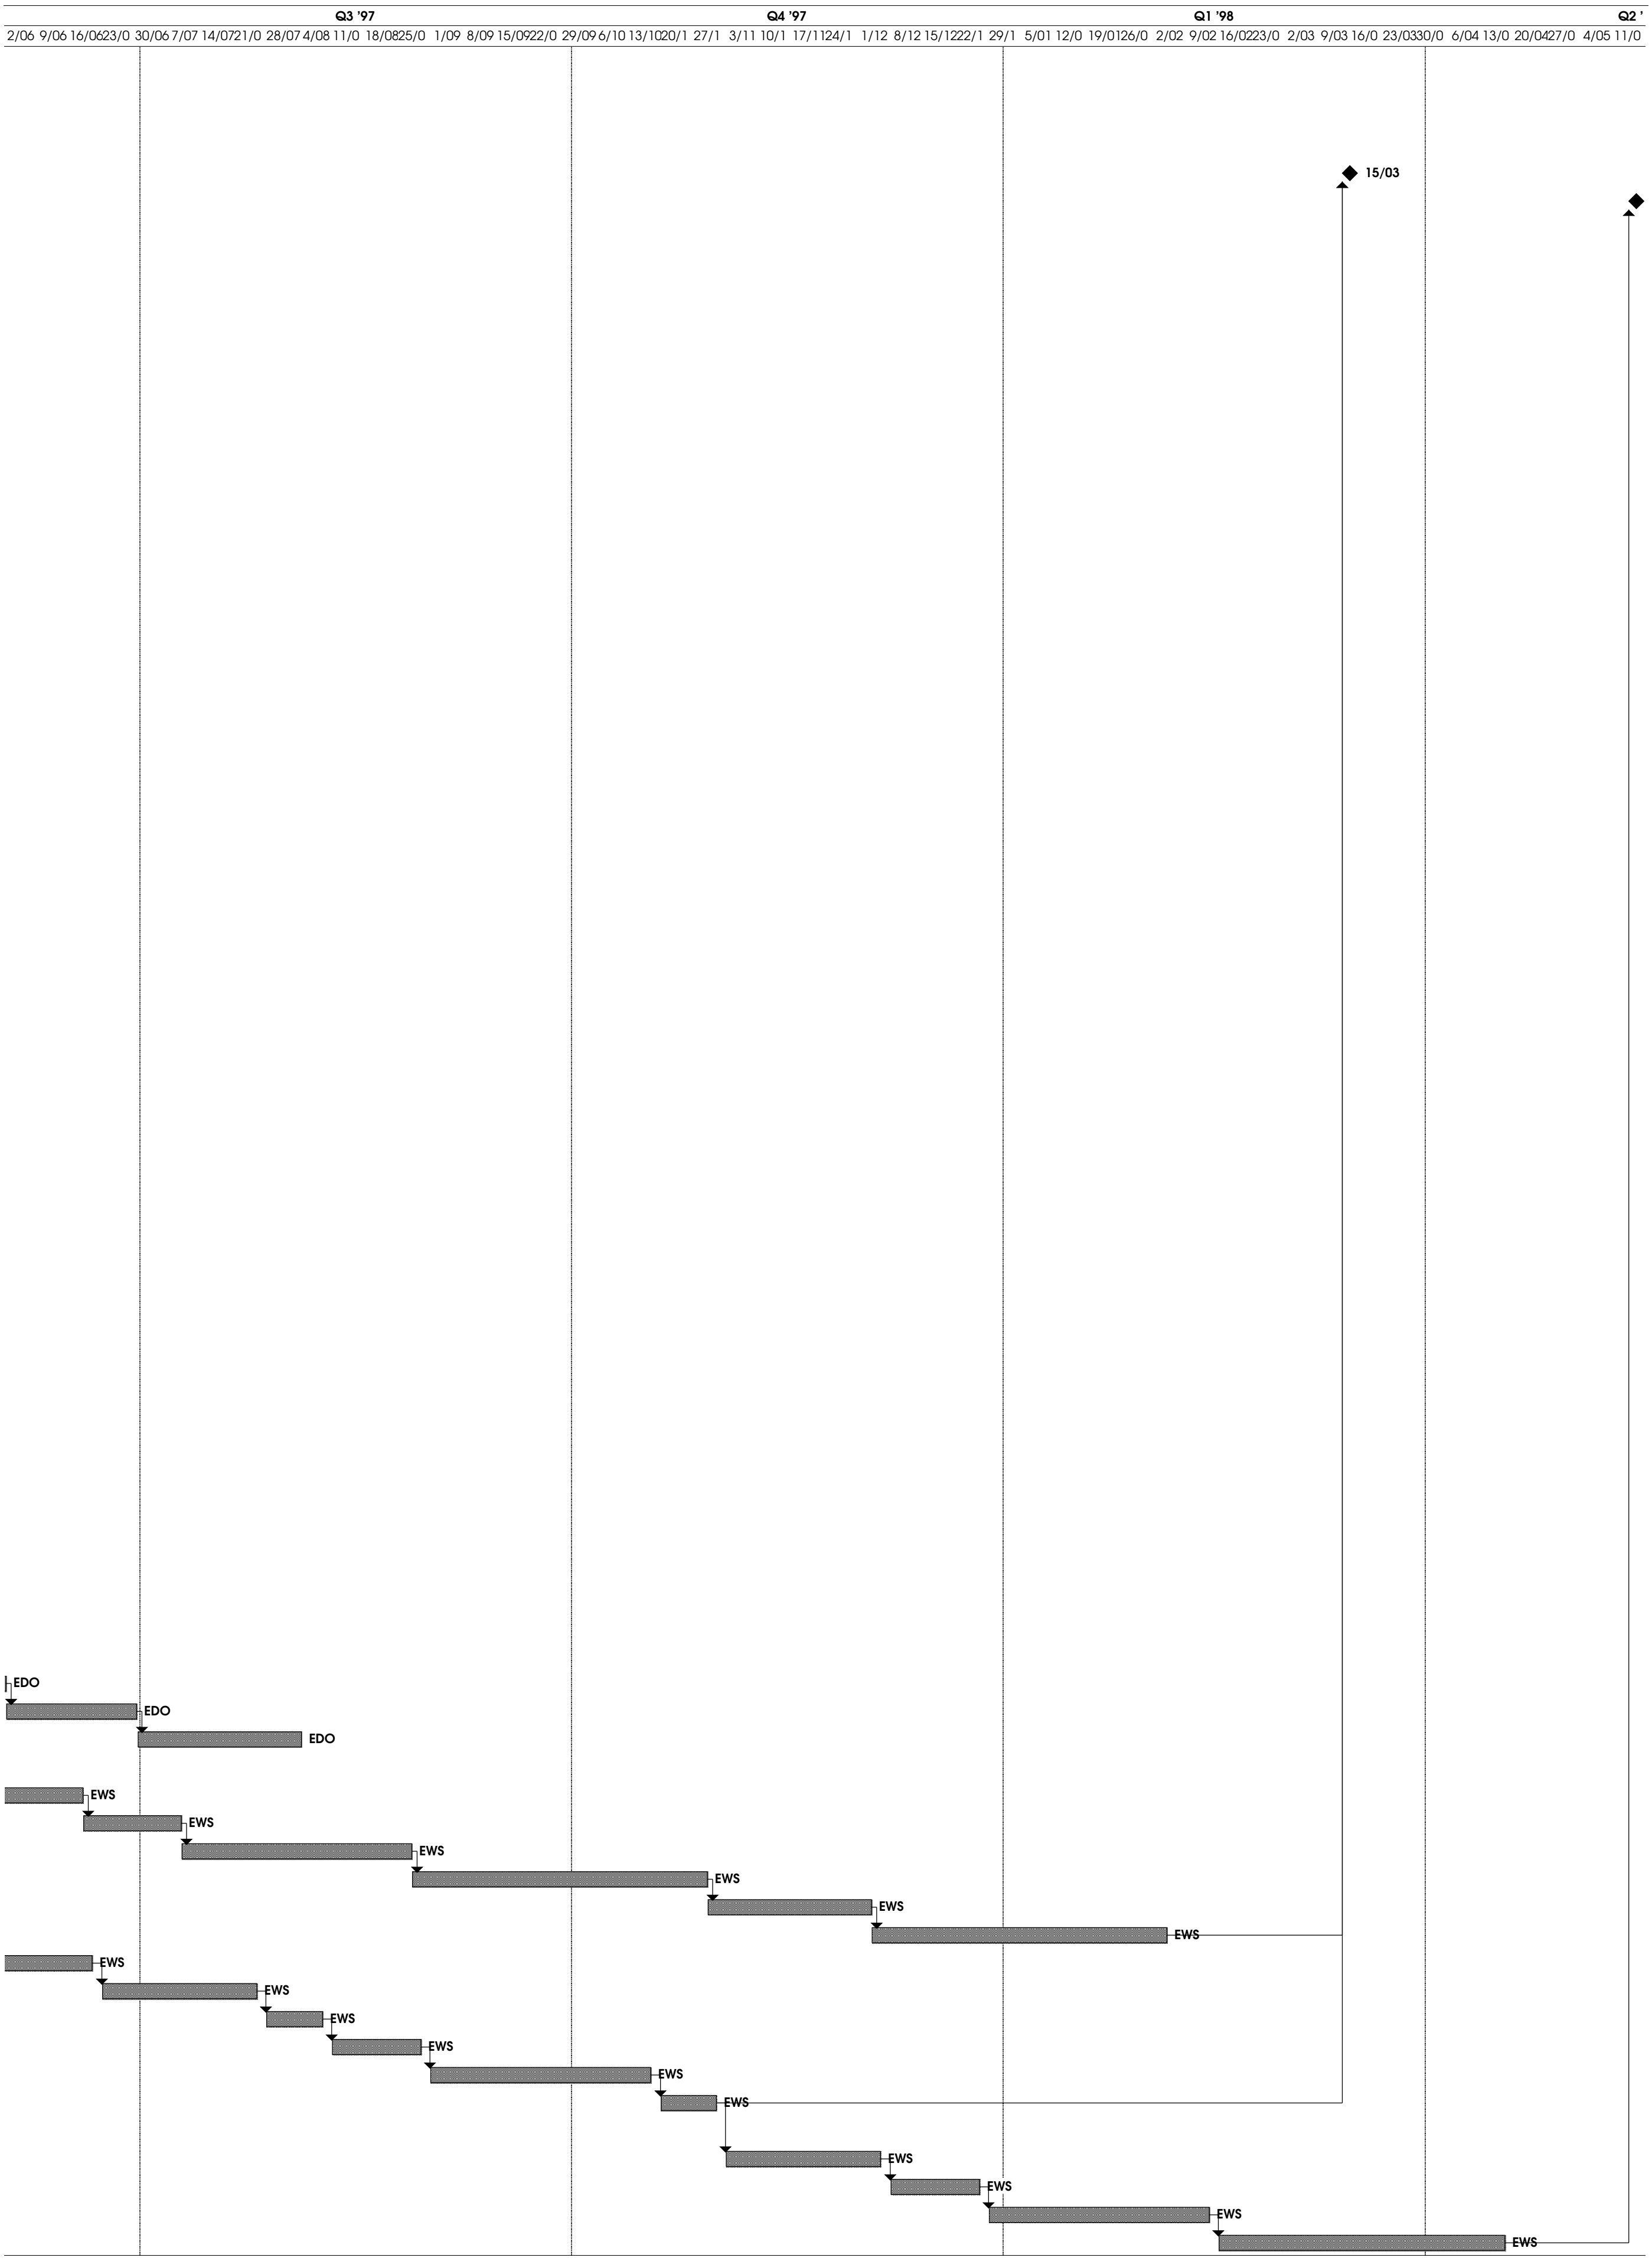

Project: XMM-OM Combined EDO and EWS
Date: 28 Oct '96

Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Milestone | Rolled Up Progress
